

Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

Date	5 September 2026
Team ID	SWUID2026190414
Project Name	Metro Ticket Generating System in ServiceNow
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation (4 Marks)

The product backlog below is based on the Metro Ticket Generating System scope: station data, ticket booking, fare calculation, QR generation, payment selection, portal UI, testing and deployment.

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Station & Ticket Setup	USN-1	As an admin, I can create and maintain metro station details so that passengers can select valid stations.	3	High	Project Team
Sprint-1	Station & Ticket Setup	USN-2	As a passenger, I can select Starting From and Going To stations from the station list.	2	High	Project Team
Sprint-1	Ticket Booking	USN-3	As a passenger, I can book a metro ticket by selecting journey type and number of passengers.	3	High	Project Team
Sprint-2	Fare Calculation	USN-4	As a passenger, I can view the fare for a single journey based on my booking details.	3	High	Project Team
Sprint-2	Fare Calculation	USN-5	As a passenger, I can view the fare for a return journey and multiple passengers.	3	High	Project Team
Sprint-2	Payment Selection	USN-6	As a passenger, I can select a payment mode such as UPI, Card or Others.	2	Medium	Project Team
Sprint-3	QR Ticket	USN-7	As a passenger, I can receive a QR-based digital ticket after submitting the booking.	3	High	Project Team
Sprint-3	QR Ticket	USN-8	As a passenger, I can view the generated QR ticket in the ServiceNow portal widget.	2	High	Project Team
Sprint-4	Security & Testing	USN-9	As an administrator, I can use table access controls for the metro station data.	2	Medium	Project Team
Sprint-4	Security & Testing	USN-10	As a project team, I can test the complete booking-to-QR flow and prepare the solution for deployment.	3	High	Project Team

Project Tracker, Velocity & Burndown Chart (4 Marks)


Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	8	6 Days	07 Sep 2026	12 Sep 2026	—	—
Sprint-2	8	6 Days	14 Sep 2026	19 Sep 2026	—	—
Sprint-3	5	6 Days	21 Sep 2026	26 Sep 2026	—	—
Sprint-4	5	6 Days	28 Sep 2026	03 Oct 2026	—	—

Velocity:

Total planned story points = 26. With a 6-day sprint duration, the planned average work rate is approximately $26 / 24 = 1.08$ story points per day across the four sprints. Sprint velocity is planned as 8, 8, 5 and 5 story points respectively.

Burndown Chart:

A burndown chart represents the work remaining against time. The chart below shows the planned remaining story points for the four sprints. Actual completion values can be entered after each sprint is completed.

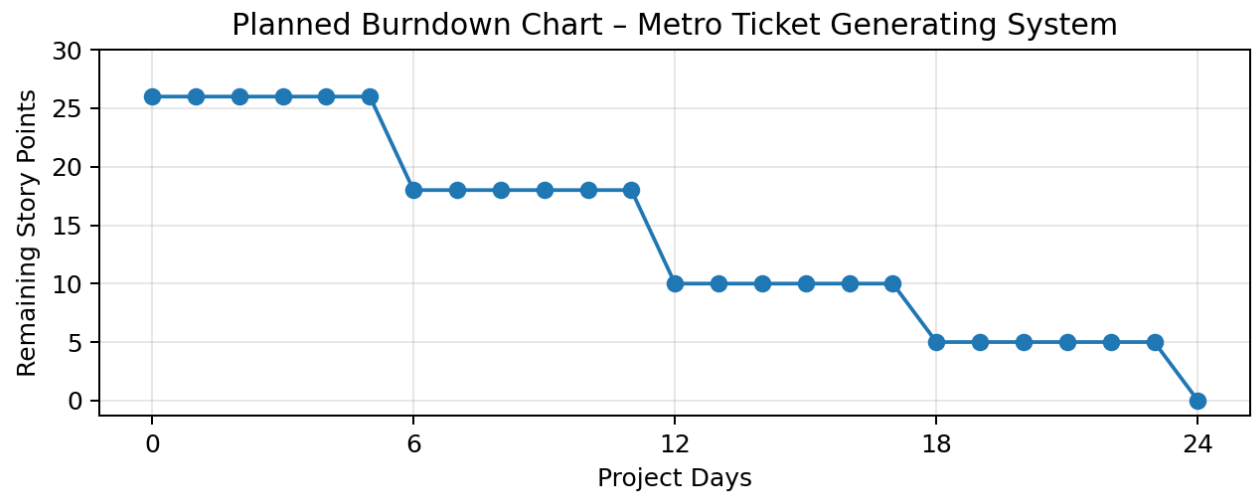

References

<https://www.atlassian.com/agile/project-management>

<https://www.atlassian.com/agile/tutorials/how-to-do-scrum-with-jira-software>

<https://www.atlassian.com/agile/tutorials/epics>

<https://www.atlassian.com/agile/tutorials/sprints>

<https://www.atlassian.com/agile/project-management/estimation>

<https://www.atlassian.com/agile/tutorials/burndown-charts>
